


Castle Top Estimating Sheet

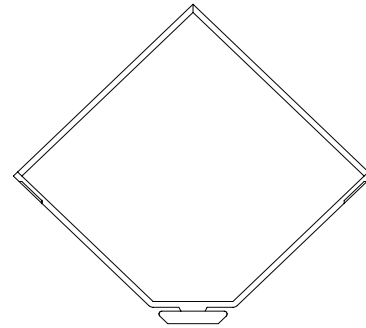

Panels

Roof Areas :

_____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 _____ x _____ = _____ sqft
 Total Roof Area = _____ sqft

Trim Components

Eave	_____	Ridge	_____
Gable	_____	Hip	_____
Headwall	_____	Sidewall	_____
Valley	_____	Shed Ridge	_____

Enter total footage required for each condition listed above

 Panel Square Footage HCT160

Total Roof Area x 1.10 = _____ sqft

Total Cartons Panel Square Footage div. by 53

_____ cartons (round to nearest full carton)

Eave

HCA112 Drip edge Eave div. by 11.5 = _____ pcs @ 12'-0"

Gable

HCA201 Gable Trim Cap Gable div. by 11.5 = _____ pcs @ 12'-0"

HCA200 Channel Trim Same qty as cap = _____ pcs @ 12'-0" →

Ridge

HCA303 Rolled Ridge/Hip cap Ridge div. by 11.5 = _____ pcs @ 12'-0"

Hip

HCA303 Rolled Ridge/Hip cap Ridge div. by 11.5 = _____ pcs @ 12'-0"

**TOTAL
HCA200**



Headwall

HCA500 Headwall Headwall div. by 11.5 = _____ pcs @ 12'-0"



Sidewall

HCA410 Sidewall Sidewall div. by 11.5 = _____ pcs @ 12'-0"

HCA200 Channel Trim Same qty as Sidewall = _____ pcs @ 12'-0"



Valley

HCA800 Valley Valley div. by 11.5 = _____ pcs @12'-0"

HCA975 Joggle Cleat HCA800 Valley x 2 = _____ pcs @ 12'-0"



Shed Ridge

HCA342 Shed Ridge Shed Ridge div. by 11.5 = _____ pcs @12'-0"

Total HCA200 Channel Trim _____

pcs @ 12'-0"

Accessories

Panel Fasteners (Choose one)

** SWR9XX 2" Painted / Gasketed Screws Total Cartons x 175 = _____ pcs (round to nearest 100)

OR

** SWR402 2" Ring Shank Grommetted Nails Total Cartons x 200 = _____ pcs (round to nearest 500)

RSS211 #12 x 1" Pancake Head Screws
(for trim installation if panels are to be fastened using SWR9XX screws)
(HCA 112 Drip Edge + HCA200 Channel Trim + HCA 975 Joggle Cleat) x 10 =
_____ pcs (round to nearest 100)

RSR3xx Rivets Total Roof Area div. by 15 = _____ pcs (round to nearest 50)

SWR9XX 2" Ptd Gasketed Screw (HSA303 Rolled Ridge/Hip x 12) + (HSA500 Headwall x 6) +
(HSA342 Shed Ridge x 12) = _____ pcs (round to nearest 100)

RSC312 Butyl Tape 50' HCA975 Joggle Cleat div. by 4.5 = _____ rolls

RSC350 Expandable Sealant Tape ((HSA303 Rolled Ridge/Hip x 2) + HSA500 Headwall +
HSA342 Shed Ridge) div. total by 1.75 = _____ pcs

RST2XX Touch up Paint 2 oz. _____ ea
